



- 1 FINALISE FUNCTIONAL SPECIFICATION
- 5 COMPLETE OPTICAL SYSTEM DESIGN
- 6 ORDER OPTICAL GLASS BLANKS
- 7 COMPLETE MECHANICAL DESIGNS
- 8 TENDER ACTION OPTICAL COMPONENTS
- 9 PLACE ORDERS FOR OPTICAL MANUFACTURE
- 10 START MANUFACTURE OF ASSEMBLYS
- 11 START MANUFACTURE OF SCIENTIFIC FIBRE BUNDLES
- 12 START DETECTOR HEAD/CAMERA CRYOGENIC ENGINEERING
- 13 START ELECTRONIC CONTROL ENGINEERING
- 14 START SYSTEM SOFTWARE
- 15 START ASSEMBLY and TESTING
- 16 DELIVERY and TESTING OF OPTICS
- 17 START FINAL TESTING AT RGO
- 18 SHIP TO La PALMA
- 19 START COMMISSIONING ON THE SKY WITH AF2
- 20 START GHRIL OPTICAL TABLE PROJECT
- 21 WAVELENGTH CALIBRATION ASSY.
- 22 FLAT FIELD ASSEMBLY
- ENGINEERING R and D

KEY DATE	COMPLETED
	OCT.88
	MARCH 91
	FEB.91
	FEB.91
	OCT.92
	AUG.92
	DEC.91
FEB.93	FEB.92
	MARCH92
SEPT.91	
NOV.92	
OCT.92	
JAN.93	
JAN.93	
NOV.92	
FEB.93	
JULY 93	
APRIL 94	
JUNE 94	
NOV.92	
COMPLETE BEFORE APRIL 94	
COMPLETE BEFORE APRIL 94	

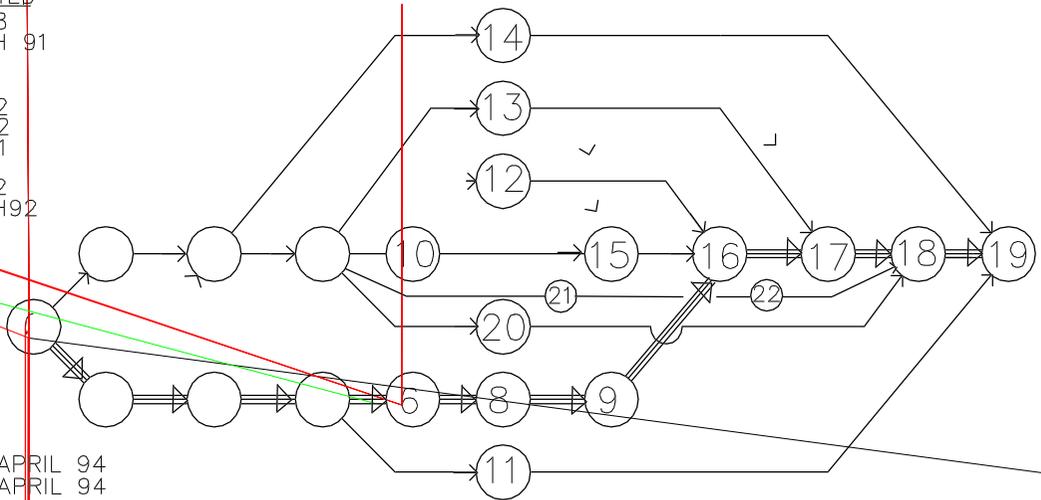

DESCRIPTION	1991				1992				1993				1994			
	J	F	M	A	J	F	M	A	J	F	M	A	J	F	M	A
	1	2	3	4	1	2	3	4	1	2	3	4	1	2	3	4
PRELIMINARY DESIGN	[Gantt bar: 1991 Q1]															
DETAIL DESIGN and MANUF DRWS.	[Gantt bar: 1991 Q1 - 1992 Q3]															
MANUFACTURE FIBRES	[Gantt bar: 1992 Q2 - 1993 Q4]															
OPTICS	[Gantt bar: 1992 Q3 - 1993 Q4]															
SOFTWARE (HIGH LEVEL VAX)	[Gantt bar: 1992 Q3 - 1993 Q4]															
ELECTRONICS and CONTROL (4ms)	[Gantt bar: 1992 Q3 - 1993 Q4]															
GHRIL OPTICAL TABLE	[Gantt bar: 1992 Q3 - 1993 Q4]															
INTEGRATION and TESTING (UK)	[Gantt bar: 1993 Q3 - 1994 Q1]															
SHIP TO La PALMA	[Gantt bar: 1994 Q1]															
COMMISSIONING	[Gantt bar: 1994 Q2]															

O-ORDER  
D-DESIGN  
M-MANUFACTURE  
A-ASSEMBLY  
T-TEST  
C-COMMISSION  
S-SHIP

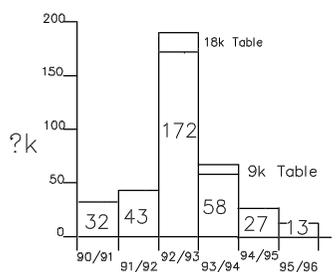

FINANCIAL PROFILE

- 3 18.12.92 DWG.
- 2 15.4.92 DWG.

ROYAL GREENWICH OBSERVATORY  
MADINGLEY ROAD  
CAMBRIDGE CB3 0EZ

Drawing No.
